

July 5, 2018

Dear Airport User/Tenant/Hangar Owner,

The Idaho Falls Regional Airport is currently reconstructing Taxiway C. This construction is the fourth phase in a multi-year Federal and Local funded grant project that includes the reconstruction/rehabilitation of Taxiway A and its associated connectors, reconfiguration of Taxiway C, and the pavement maintenance and re-numbering of Runway 02-20.

In this letter we have provided an overview of the construction work zones for the next phases of the project as well as planned vehicle routes and haul roads to be used by construction teams. We hope you will utilize this information as part of your local flight plan to ensure operational safety during taxi or other ground operations on or adjacent to the work areas.


Closures will be posted via the Notice to Airmen (NOTAM) system, and the dates below are tentative based on factors such as the contractors' progress, weather, and other unforeseen issues that may speed up or delay work on this project. Please check NOTAMs frequently as conditions may change rapidly and with little notice.

Phase 4 is currently underway as noted on the map below (construction vehicle routes are depicted with a yellow arrow):



This phase is currently scheduled from now through July 24, 2018.

Phase 5 is depicted on the map below:

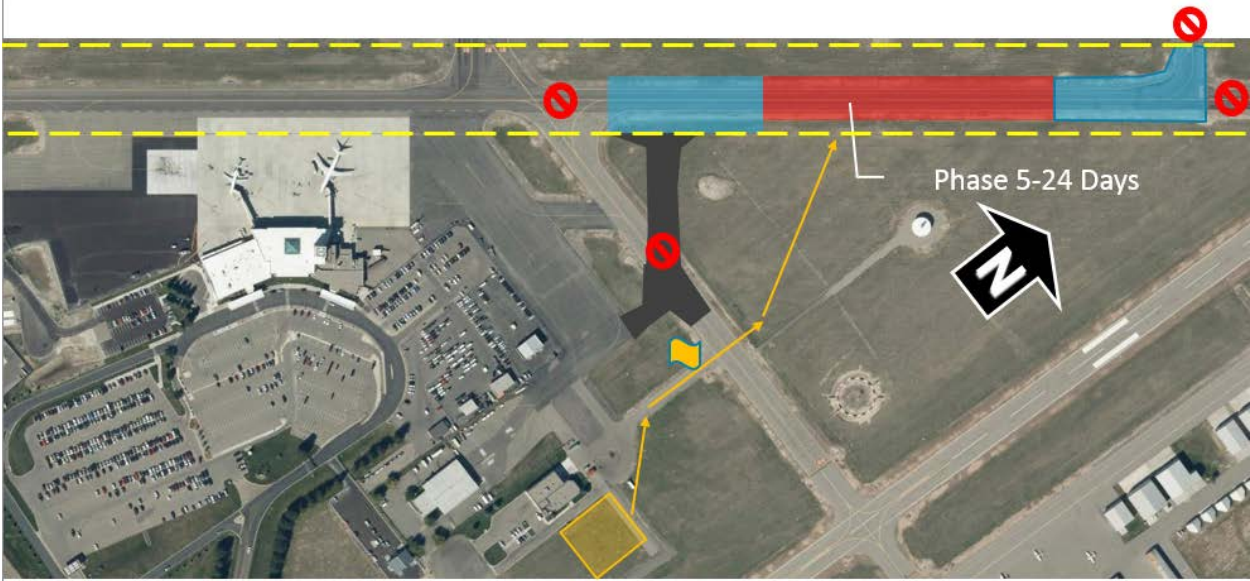


This phase is tentatively scheduled for July 25, 2018 – August 17, 2018.

Phase 6 is broken into 3 sub-phases - Phases 6A, 6B, and 6C are depicted on the map below:



Phase 6A is tentatively scheduled August 18, 2018 – August 31, 2018

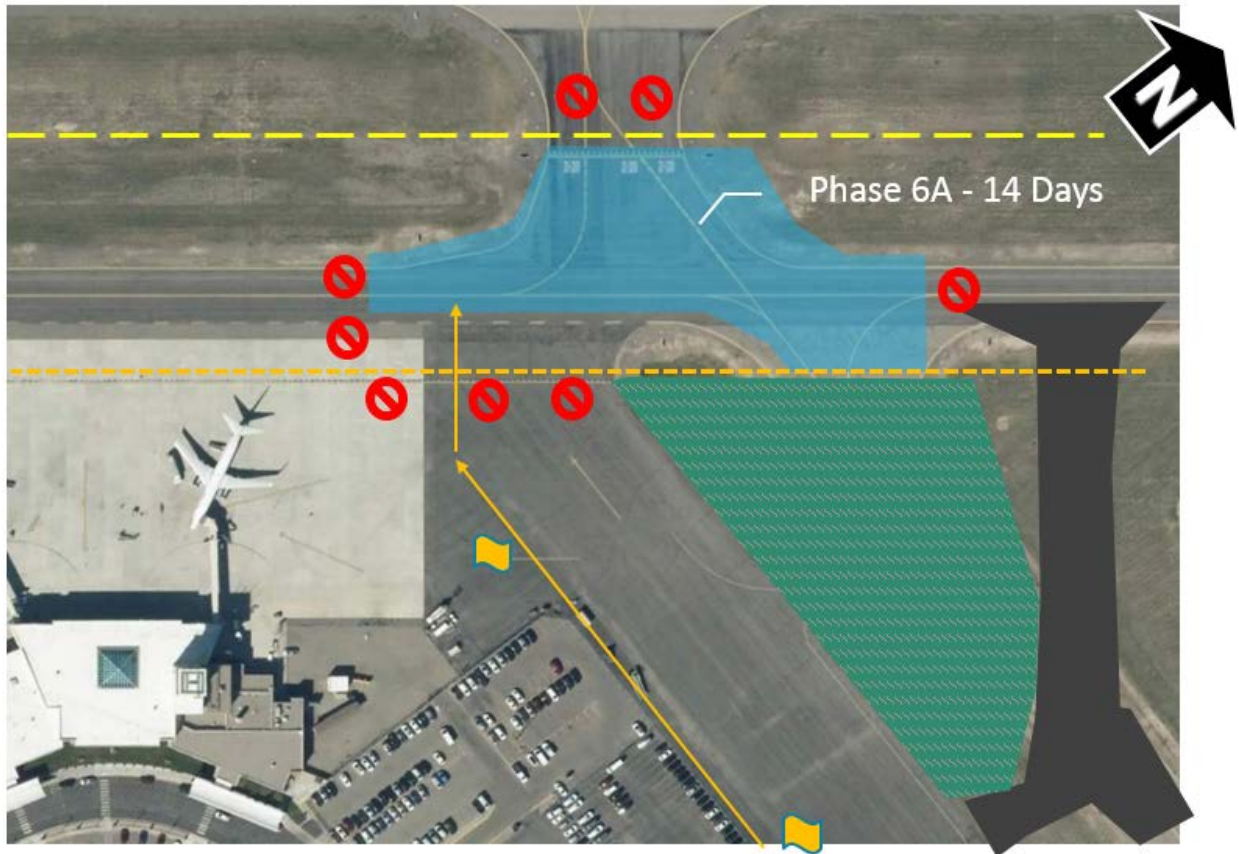

Phase 6B is scheduled for September 5, 2018 – September 10, 2018



PHASE 6B includes the **CLOSURE** of Runway 2-20 from Sept. 5 through Sept. 10. The runway will be **CLOSED** to **ALL** aircraft operations during this time. Aircraft will have access to Runway 17-35 during the closure.

Operations on all **OPEN** taxiways and Runway 17-35 will be directed by ATCT during normal operating hours.

CTAF (118.5) must be used when ATCT is unavailable.

Phase 6C is scheduled for September 11, 2018 – September 15, 2018



Phase 7 is scheduled for September 16, 2018 – September 25, 2018



The safety of the construction team, ground vehicle operators, and the Airport users is the utmost priority and we appreciate your cooperation and support while we continue to make these critical improvements to the infrastructure at IDA!

If you have any questions, please contact Airport Operations at 208-612-8267.

